Agile_EventManagement_ProjectPlan_4000w

by Agile_eventmanagement_projectplan_4000w

Agile_eventmanagement_projectplan_4000w

Submission date: 26-Mar-2026 10:35PM (UTC-0700)
Submission ID: 2914447719
File name: Agile_EventManagement_ProjectPlan_4000w.docx (1.1M)
Word count: 4178
Character count: 24880

PROJECT MANAGEMENT PLAN

Agile Event Management Project

A Scrum-Based Framework for End-to-End Event Delivery

Student Name: _____

Student ID: _____

Course / Unit: Project Management

Submission Date: _____

Table of Contents

The sections below constitute the full project management plan. Page numbers update automatically in Microsoft Word (right-click → Update Field).

No.	Section
1	Executive Summary
2	Business Case
3	Project Scope
4	Milestones
5	Change Management Plan
6	Communication Management Plan
7	Cost Baseline
8	Procurement Plan
9	Risk Management Plan
10	Risk Register
11	Quality Standards and Acceptance Criteria
12	Work Breakdown Structure (WBS)
13	Gantt Chart
14	Network Diagram
15	Resource Allocation
16	Budget and Estimation
17	Critical Analysis
18	References
19	Appendices

1. Executive Summary

The Agile Event Management Project is an official project to plan, design, acquire, rehearse, implement, and critique a multi-day corporate or public event, accomplished in six Scrum sprints of iterative work, over a period of a hundred and sixty weeks. The project team includes twelve resource roles with the Project Manager, Scrum Master, and Event Director at its core and with expert functions of the marketing, graphics design, logistics, audiovisual production, catering, and finance functions. The general aim is to achieve high quality event that will meet the strategic objective of the client in terms of the experience of attendees, commercial performance and regulatory performance (Bowdin et al., 2011). The timeline is anchored by three formal milestones, including Council Permit Approval, Venue Confirmed, and Ticket Sales Launch. AUD $391,100 has been approved as a cost baseline covering human resource cost of AUD 247,040, external procurement cost of AUD 108,500 and a 10 percent contingency cost of AUD 35,554.

2. Business Case

This complexity in dealing with concurrent work streams in venue procurement, supplier interaction, marketing implementation, regulatory compliance, and on-site operations is why formal project management governance is required (Kerzner, 2022). In the absence of a well-planned approach, projects of this magnitude can be susceptible to scope creep, cost overruns and loss of coordination which can significantly affect the reputation and business performance of the client. Agile-Scrum was chosen instead of a traditional waterfall system due to the flexibility of the iterative sprint model to meet the constantly changing nature of creative and marketing decisions without losing control of timely contractual and regulatory implementation (Schwaber and Sutherland, 2020). The visibility that is provided by each sprint review meeting to the client is structured and has a formal meeting with the client to approve deliverables and refine the backlog before the next sprint is initiated which makes sure that the project is delivered according to the changing stakeholder expectations during the delivery lifecycle. The main stakeholder groups are the client organisation, attendees, sponsors, suppliers, as well as regulatory authorities, all of which will be gaining different values with the professional management of this project.

3. Project Scope

The project scope involved all undertakings in between the project charter development up to formal closure, such as the establishment of the Scrum framework, event concept and brief definition, regulatory and compliance planning, venue selection and contracting, procurement of all core suppliers, event branding and creative development, the marketing campaign implementation, the ticketing operation, and the attendee management, the schedule of logistics and production, staffing and volunteer management, the health and safety planning, a complete technical rehearsal, the entire operation of the event to a maximum of two days and the post event financial reconciliation and evaluation. Out of scope are the continuous post-event marketing activities that take longer than the thirty calendar days, permanent change in venue infrastructure and any timelines in the regulating decision making that are not under the control of the project team. The project is run on the assumption that the event will be hosted at a single venue, the client will also supply approvals on time during the sprint review and finally all the permits and licences will be availed within the timelines. The only major limitations are the set event date that promotes all the reverse scheduling and approved budget limit of AUD 391,100, which is aligned with the scope limits suggested by Larson and Gray (2021).

4. Milestones

The MS Project schedule has three zero-duration milestone tasks that serve as dependency gates to downstream activities (Larson and Gray, 2021). The sprint review meeting is also an informal milestone as each of the meetings represents the approval of the sprint deliverables by the client and the permission to continue.

Milestone	Phase	Gated Activities
Council Permit Approval Received	Initiation	All public-facing activities, venue setup, and supplier confirmations requiring regulatory clearance.
Venue Confirmed	Sprint 1	Floorplan design, production scheduling, logistics planning, and AV specification.
Ticket Sales Launch	Sprint 2	Attendee registration monitoring, VIP management, confirmation emails, and dietary data collection.
Sprint 5 Review Sign-Off	Sprint 5	Event execution sprint commencement — all rehearsals and venue setup confirmed complete.
Project Sign-Off and Archiving	Closure	Formal client acceptance of final closure report, lessons learned register, and financial reconciliation.

5. Change Management Plan

Any amendments to the approved project baseline should be presented in a formal Change Request Form, which includes the description of the nature of the change, the affected elements of the baseline, the rationale and the approximate schedule, cost, and quality effects (PMI, 2021). The Project Manager will have the delegated powers to authorize changes that have a cost impact of less than AUD $5,000 and a schedule impact less than three working days, but will not change the event idea, the core supplier contracts or any major regulatory obligations. Alterations that are above these amounts are made before the Change Control Board, which includes the Project Manager, Event Director, Finance Manager and the Client who must meet within a span of five working days and make a formal decision in writing. The revised plan of project, updated cost baseline and revised communications plan all capture all the approved changes. Agile framework also supports backlog refinements and sub-task changes that occur during sprint retrospectives by making minor amendments to standard sprint planning, but they are not subject to a formal change request unless they impact the approved scope, budget, and event concept (Schwaber and Sutherland, 2020).

6. Communication Management Plan

One of the best predictors of project success is effective communication where all the stakeholders are informed correctly, promptly and with the necessary details (Heldman, 2018). The project will use weekly status reports to the entire core team and the client, weekly sprint planning, and weekly sprint review with the client present at the end of every sprint, daily fifteen-minutes standups throughout Sprint Six, and formal supplier briefing documents at major procurement and production milestones.

Stakeholder	Information Need	Channel	Frequency	Responsible
Client Organisation	Progress, budget, risks, sprint reviews.	Email, sprint reviews.	Weekly + per sprint.	Project Manager.
Project Team	Task assignments, sprint priorities, blockers.	Standups, sprint planning.	Daily / per sprint.	Scrum Master.
Venue Management	Event specs, bump-in schedule, site access.	Email, briefing documents.	At contract and pre-event.	Event Director.
Suppliers	Contract terms, technical specifications, delivery confirmations.	Email, supplier briefing documents.	At contracting and pre-event.	PM / Event Director.
Attendees	Registration confirmation, programme logistics.	Email campaigns, website, social media.	Pre-event and post-event.	Marketing Coordinator.

7. Cost Baseline

The cost baseline is a ratified, time-staggered budget on which the actual spending is planned and regulated throughout the project lifecycle (PMI, 2021). It was created by a bottom-up estimation method, which consolidated the work breakdown structure task-level cost estimations of the MS Project. The approved budget has a contingency reserve of ten percent AUD 35,554 in it, which is within the recommendation of Kerzner (2022) of projects with moderate risk profiles.

Budget Category	Estimated Cost (AUD)	% of Total	Notes
Human Resource Costs	$247,040	63.2%	11 paid resource roles × estimated days × hourly rate.
External Procurement Costs	$108,500	27.7%	Venue, catering, AV, entertainment, marketing, logistics.
Permits, Licences, and Insurance	$8,000	2.0%	Council permit, liquor licence, public liability insurance.
Contingency Reserve (10%)	$35,554	9.1%	Risk and uncertainty buffer.
TOTAL PROJECT BUDGET	**$391,100**	**100%**	**Approved cost baseline.**

8. Procurement Plan

Procurement management assures that any external goods and services are procured by a process which is best value providing and which creates clarity and commitment in the contract (Kerzner, 2022). The procurement strategy embraces the competitive quotation procedure in all large types of expenditures, and a minimum of three written quotations must be received and then the contract is awarded. Venue hires the most important single procurement, is handled by a formal site visit and the negotiation with the contract specifying the clause of cancellation and liability. Each of the contracts of catering, audiovisual, entertainment and photography contain the performance specifications, penalty in material failure, and final confirmation procedures in accordance with the project schedule.

Category	Method	Contract Type	Est. Cost (AUD)	Responsible
Venue Hire	Competitive shortlist.	Fixed price hire agreement.	$22,000	Project Manager.
Catering Services	Tasting and selection.	Fixed price per head.	$18,000	Event Director.
Audiovisual Production	Technical rider + quotation.	Fixed price AV services.	$8,500	AV Technician.
Entertainment / Performers	Client-directed selection.	Performance contract.	$12,000	Event Director.
Photography & Videography	Portfolio review.	Day-rate services contract.	$5,500	Event Director.
Furniture, Staging & Rigging	Competitive quotation.	Hire agreement.	$13,000	Logistics Coordinator.
Security and First Aid	Accredited provider quotation.	Day-rate services contract.	$6,000	Project Manager.
Paid Marketing and Print	Marketing strategy allocation.	Campaign spend / print order.	$12,500	Marketing Coordinator.
Ticketing Platform	Platform configuration.	SaaS subscription.	$1,500	Project Manager.
Merchandise and Gifts	Competitive quotation.	Supply purchase order.	$4,000	Marketing Coordinator.
TOTAL EXTERNAL PROCUREMENT			**$108,500**	

9. Risk Management Plan

Risk management refers to the systematised procedure of determining, evaluating, strategizing on how to respond to, and monitoring risks in order to maximise good results and reduce the adverse effects (PMI, 2021). This project assumes the use of a four-step risk cycle, namely identification, assessment, response planning and monitoring, throughout all the sprints. Risk identification is done at the beginning of the sprint by conducting facilitated team workshops, supplier contribution, regulatory direction, and post facto discussions. Through risk assessment, a five by five qualitative probability-impact matrix is used; the scores obtained 1-4 Low, 5-9 Moderate, 10-16 High, 17 to 25 critical. Response plans of all the High and Critical risks should be formally documented and assigned to a risk owner. There exist four strategies of response, which include avoidance, mitigation, transference and acceptance. The nature and cost-effectiveness of the available response options help to select the appropriate strategy; it is consistent with the strategy suggested by O'Toole (2011) to manage the risk of event management.

10. Risk Register

Risk Description	Prob.	Impact	Score	Owner	Response
Venue cancellation after contract execution.	Low (2)	Critical (5)	**10 – High**	Project Manager.	Transfer: Venue cancellation insurance; financial penalty clauses in contract.
Council permit rejection or delay.	Mod. (3)	High (4)	**12 – High**	Project Manager.	Mitigate: Submit application with four-week buffer; ongoing liaison with council.
Key supplier withdrawal before event day.	Mod. (3)	High (4)	**12 – High**	Event Director.	Mitigate: Maintain pre-qualified back-up supplier list; contractual cancellation penalties.
Budget overrun from scope changes or cost escalation.	Mod. (3)	Mod. (3)	9 – Mod.	Finance Manager.	Mitigate: Formal change control process; monthly budget-to-actual reporting; 10% contingency reserve.
Scope creep from uncontrolled client change requests.	High (4)	Mod. (3)	**12 – High**	Project Manager.	Avoid: Enforce formal change request process; document approved baseline at initiation.
AV technical failure during live programme delivery.	Low (2)	High (4)	8 – Mod.	AV Technician.	Mitigate: Full technical rehearsal; backup equipment provisions in AV contract.
Health or security incident during event.	Low (2)	Critical (5)	**10 – High**	Event Director.	Mitigate: Risk assessment, emergency evacuation plan, first aid, and security all contracted in-scope.
Low ticket sales impacting event revenue.	Low (2)	High (4)	8 – Mod.	Mktg Coordinator.	Mitigate: Multi-channel marketing campaign; early-bird pricing; influencer outreach.

11. Quality Standards and Acceptance Criteria

In this project, quality management will include quality project management process and quality event delivery results (PMI, 2021). There are five dimensions in which the quality standards are set including the stakeholder satisfaction, programme delivery, supplier performance, regulatory compliance, and financial accuracy. The post-event attendee survey should have an overall mean score of experience of 4.0 or better on a five-point Likert scale. The sessions of all programmes should start within five minutes of the publicity. The suppliers contracted should all undergo pre-event briefing sessions and sign a written commitment of delivery before any activity that involves publicly facing can be undertaken. Financial accuracy stipulates that all the expenditure must be recorded against proper budget line and all supplier invoice must be reconciled and paid.

Deliverable	Acceptance Criteria	Review Point
Project Charter	Signed and dated by Project Manager and Client.	Initiation.
Regulatory Permits and Licences	All permits and licences received in writing before any public-facing activity commences.	Sprint 1 review.
Venue and Supplier Contracts	Signed contracts for venue, catering, AV, entertainment, and photography; each specifying price, scope, and cancellation terms.	Sprint 1–2 reviews.
Event Branding and Collateral	All branding deliverables reviewed and approved by the client in writing.	Sprint 2 review.
Technical Rehearsal	Full technical run-through completed with no unresolved critical AV or staging issues.	Sprint 5 review.
Event Day Delivery	All programme sessions delivered per the approved run sheet; no critical safety or operational incidents unresolved.	Sprint 6 review.
Post-Event Survey	Minimum 30% response rate; overall satisfaction mean ≥ 4.0 / 5.0.	Project Closure.
Financial Reconciliation	Final budget-to-actual variance within ±10% of approved baseline; all invoices reconciled.	Project Closure.
Project Closure Report	Post-event evaluation report, lessons learned register, and final budget report signed off by PM and Client.	Project Closure.

12. Work Breakdown Structure (WBS)

WBS Work Breakdown Structure is a hierarchical breakdown of the overall project scope into sequentially smaller units that form the basis of scheduling, estimation of costs, resources, and risks management (PMI, 2021). The WBS has been created in Microsoft project under three outline levels. Level 1 describes the eight main project stages; Level 2 is the description of the large work packages at each stage and Level 3 is the description of small tasks with the duration, resource allocation, and predecessor relationships. The complete WBS export of Microsoft project is included in Appendix A. The Level 1 and Level 2 summary structure is as shown below.

ID	Phase / Work Package	Key Tasks
1.0	**Project Initiation & Foundation**	Project charter; Scrum setup; event concept and brief; regulatory and compliance planning.
2.0	**Sprint 1: Venue & Supplier Procurement**	Sprint planning; venue selection, site visits, negotiation, and contract; catering, AV, entertainment, photography bookings.
3.0	**Sprint 2: Event Design & Creative**	Event branding; signage; stage and floorplan design; marketing strategy; website; social media; ticketing and registration.
4.0	**Sprint 3: Logistics & Production Planning**	Master run sheet; supplier briefs; equipment hire; staffing and volunteer recruitment; health, safety, and security planning.
5.0	**Sprint 4: Marketing Execution & Sponsor Management**	Paid ads; email campaigns; press releases; sponsor contracts; branding integration; attendee management.
6.0	**Sprint 5: Final Production & Rehearsal**	Final supplier confirmations; staff training; AV and staging rehearsal; full technical run-through; bump-in and venue setup.
7.0	**Sprint 6: Event Execution**	Event day operations Days 1 and 2; guest registration; programme delivery; catering; networking; incident management.
8.0	**Project Closure & Evaluation**	Bump-out; post-event marketing; feedback surveys; financial reconciliation; lessons learned workshop; project sign-off.

13. Gantt Chart

Microsoft project was used to create and construct the project schedule in the form of a Gantt chart that represents the entire sixteen-week project lifecycle, all task bars, predecessor dependency lines, milestone diamonds, and resource assignments (Larson and Gray, 2021). The chart is organized into the phase bands which are aligned with the eight project phases and allow one to identify the sprint boundaries and the milestones date at a glance. The initiation phase will take the first two weeks, where the Sprint one will begin as soon as the project charter is signed. Sprints Two to five are around two to three weeks each. Sprint Six will be in line with the event day and the project closure phase will last about three weeks after this to allow financial reconciliation and the final evaluation report. All the Gantt chart items of the Microsoft Project are attached in Appendix B.

14. Network Diagram

It was created using the predecessor relationships as specified in the MS Project schedule, which shows the logical sequencing of all the project tasks of approximately 190 in a directed acyclic graph and allows the determination of the critical path, float of the non-critical activities, and key convergence and divergence nodes (Lock, 2020). The most vital convergence point is the Council Permit Approval milestone where three parallel regulatory activities, namely, council event permit, liquor licence, and public liability insurance, have to be completed before downstream activities can commence. The Venue Confirmed milestone is a significant divergence node where several Sprint Two and Sprint Three workstreams converge at the same time such as the design of the floorplan, development of the production schedule, and booking of equipment. The float analysis will establish that the activities within post-event marketing and feedback will be of the most flexible nature in terms of timing, and as such, these are capable of introducing buffer capacity to absorb event-day delays during the time of closure. Appendix C shows the entire network diagram.

15. Resource Allocation

The allocation of the resources was controlled with the use of the assignment feature of Microsoft Project, which allows the Project Manager to identify the overallocation and implement resource levelling when needed to create the feasible schedule (Meredith et al., 2017). There are twelve types of resources found in the project, which include eleven paid human resource positions and the non-paid client stakeholder. The greatest allocation is on the Project Manager along the project lifecycle that includes sprint planning, negotiations with suppliers, regulatory compliance, risk management and closure of the project.

Resource	Rate (AUD/hr)	Est. Days	Est. Cost (AUD)	Primary Role
Project Manager	$120	80	$76,800	Overall accountability.
Event Director	$110	60	$52,800	Creative and operational leadership.
Scrum Master	$100	40	$32,000	Sprint facilitation.
Finance Manager	$100	15	$12,000	Budgeting and reconciliation.
Marketing Coordinator	$85	40	$27,200	Marketing, ticketing, attendee comms.
Graphic Designer	$80	20	$12,800	Branding and collateral.
Logistics Coordinator	$80	20	$12,800	Equipment and bump-in/out.
AV Technician	$90	10	$7,200	AV, staging, and rehearsal.
Venue Manager	$85	8	$5,440	Venue liaison and facilities.
Catering Manager	$75	8	$4,800	F&B service on event days.
General Staff	$40	10	$3,200	Event day setup and registration.
Client	$0	N/A	$0	Approvals and sign-offs.
TOTAL HR COST		**311 days**	**$247,040**	

16. Budget and Estimation

The project budget has been formulated based on the bottom-up estimation method, which constitutes the estimates of the cost of separate work packages at task stages and consolidation of these to generate phase and total project cost values (Larson and Gray, 2021). The rationale behind the choice of this approach is that the degree of task-level detail that can be obtained in the MS Project schedule gives the level of granularity needed to perform accurate resource-level cost estimation, and because bottom-up estimation is recognized as the most accurate of the three main estimation methods - analogous, parametric, and bottom-up - in situations where a developed WBS exists (PMI, 2021).

Project Phase	HR Cost (AUD)	External Cost (AUD)	Phase Total (AUD)
Project Initiation & Foundation	$20,160	$8,000	$28,160
Sprint 1: Venue & Supplier Procurement	$32,000	$55,000	$87,000
Sprint 2: Event Design & Creative	$38,400	$10,500	$48,900
Sprint 3: Logistics & Production Planning	$28,800	$15,000	$43,800
Sprint 4: Marketing Execution & Sponsor Mgmt	$32,000	$9,000	$41,000
Sprint 5: Final Production & Rehearsal	$28,160	$6,000	$34,160
Sprint 6: Event Execution	$30,400	$5,000	$35,400
Project Closure & Evaluation	$37,120	$0	$37,120
Project Subtotal	**$247,040**	**$108,500**	**$355,540**
Contingency Reserve (10%)			$35,554
TOTAL APPROVED BUDGET			**$391,094**

17. Critical Analysis

17.1 Agile-Scrum in an Event Management Context

The utilization of Agile-Scrum in this event management project is an intentional shift away of traditional waterfall methods of event delivery that has historically controlled event delivery practice (Bowdin et al., 2011). Waterfall approaches are very strict and follow a strong sequential sequence based on requirement, design, execution, evaluation which leaves the project team highly limited in terms of being able to accommodate changes in preferences of the stakeholders or changes in the market environment. The Scrum sprint framework offers this shortcoming using time-bound periods of productive development separated by client inspection and backlog purification. The assumption of Scrum is the unpredictability of complex problems to be fully planned in the beginning and that empirical process control, transparency, and adaptation is the only possible form of governance of complex endeavours, according to Schwaber and Sutherland (2020). The six sprint review meetings within this project plan will provide at least six formalized client feedback chances within the sixteen weeks of delivery, which is essentially essential in the development of alignment and eliminating the probability of late-stage scope conflicts.

The use of Scrum in event management has its limitations, however. The framework was designed to develop software products, the deliverables are digital, the iterative development process is technically easy and no point of no return in the development provides all the delivery risk (Highsmith, 2009). Most of the deliverables in event management are time-constrained (contracts with the venue, permits granted by the regulatory bodies), legally binding, or physically non-reversible in nature, which is an initial constraint on the adaptive flexibility offered by Scrum in theory. This plan includes resolving this tension by being a hybrid, Scrum ceremony structure when it comes to engaging clients and coordinating the team, but introducing hard sequence dependencies within the MS Project schedule when it comes to all contractual and regulatory work. This practical stance is indicative of the fact that there is no perfect methodology that would be applicable in the complexity of an actual event management project.

17.2 Estimation and Budgeting

The bottom-up estimation method provides traceable internally consistent cost estimates based on actual task-level scope of work that facilitates the monitoring and variance analysis of costs to be meaningful across the project lifecycle. One serious weakness, though, is that it is sensitive to the completeness and accuracy of the WBS (Larson and Gray, 2021). When the WBS is underestimating effort in highly variable areas (sponsor negotiations, regulatory approval schedules, or technical rehearsal complexity) the risk of systematic underestimation in the budget will be absorbed by the ten percent contingency reserve only partially. Kerzner (2022) suggests medium-risk projects to have contingency reserves of between five and fifteen percent, so the reserve that was taken in this case is fair, although is at the lower end of reasonable practice in terms of a multi-supplier, public-event delivery. The weakness of the budget would be overcome by sensitivity analysis of the key cost drivers and this would help to build the credibility of the budget at subsequent stages.

17.3 Communication and Stakeholder Management

The communication and stakeholder management are present in the 17.3 section. The stakeholder communication matrix that is explicitly formulated by this project identifies what information is required and via which channel, how often, and by whom each group of stakeholders is to receive the information,

establishing a written accountability of the communication requirements that can be tracked and implemented. According to Heldman (2018), communication planning is among the least heavily funded aspects in project management, and communication breakdowns explain the disproportionality of project delays and dissatisfaction outcomes to stakeholders. The obligatory involvement of the client during the sprint review meetings is the one of the most essential design attributes, which guarantee that the project team will get formal client feedback not once in a project delivery milestone, but on a consistent basis. The daily standup organization of the Sprint Six also helps in real-time coordination on the event day so that the Project Manager can surface and overcome operational problems within a shorter decision-making dissimilarity where the cost of not acting is most vital.

18. References

Bowdin, G., Allen, J., O'Toole, W., Harris, R. and McDonnell, I. (2011) *Events Management*, 3rd edn. Oxford: Butterworth-Heinemann.

Heldman, K. (2018) *PMP: Project Management Professional Exam Study Guide*, 9th edn. Indianapolis: Sybex.

Highsmith, J. (2009) *Agile Project Management: Creating Innovative Products*, 2nd edn. Boston: Addison-Wesley.

Kerzner, H. (2022) *Project Management: A Systems Approach to Planning, Scheduling, and Controlling*, 13th edn. Hoboken: Wiley.

Larson, E.W. and Gray, C.F. (2021) *Project Management: The Managerial Process*, 8th edn. New York: McGraw-Hill.

Lock, D. (2020) *Project Management*, 11th edn. London: Routledge.

Meredith, J.R., Shafer, S.M. and Mantel, S.J. (2017) *Project Management in Practice*, 6th edn. Hoboken: Wiley.

O'Toole, W. (2011) *Events Feasibility and Development: From Strategy to Operations*. Oxford: Butterworth-Heinemann.

Project Management Institute (PMI) (2021) *A Guide to the Project Management Body of Knowledge (PMBOK® Guide)*, 7th edn. Newtown Square: PMI.

Schwaber, K. and Sutherland, J. (2020) *The Scrum Guide: The Definitive Guide to Scrum: The Rules of the Game*. Scrum.org. Available at: https://scrumguides.org (Accessed: 1 March 2025).


19. Appendices


Appendix A — Work Breakdown Structure (MS Project Export)


GANTT CHART


	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Add New Column
1		Project Initiation & Foundation	11 days	Wed 01/04/26	Wed 15/04/26			
22		Sprint 1: Venue and Supplier Procurement	21 days	Wed 01/04/26	Wed 29/04/26			
44		Sprint 2: Event Design and Creative	22 days	Wed 01/04/26	Thu 30/04/26			
68		Sprint 3: Logistics and Production Planning	16 days	Wed 01/04/26	Wed 22/04/26			
94		Sprint 4: Marketing Execution and Sponsor Management	15 days	Wed 01/04/26	Tue 21/04/26			
118		Sprint 5: Final Production and Rehearsal	18 days	Wed 01/04/26	Fri 24/04/26			
144		Sprint 6: Event Execution	24 days	Wed 01/04/26	Mon 04/05/26			
170		Project Closure and Evaluation	23 days	Wed 01/04/26	Fri 01/05/26			


Appendix B — Gantt Chart (MS Project Export)

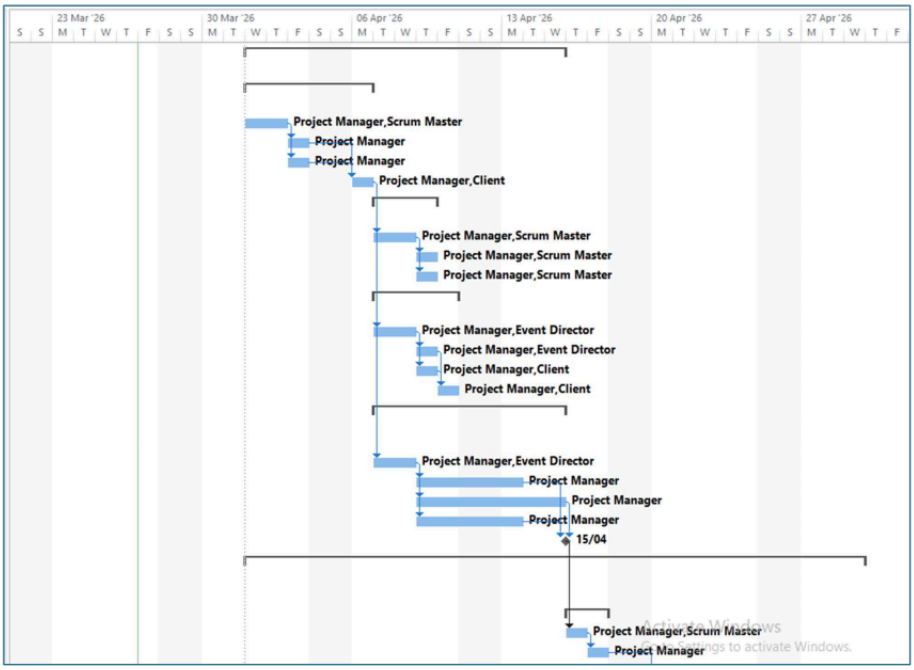


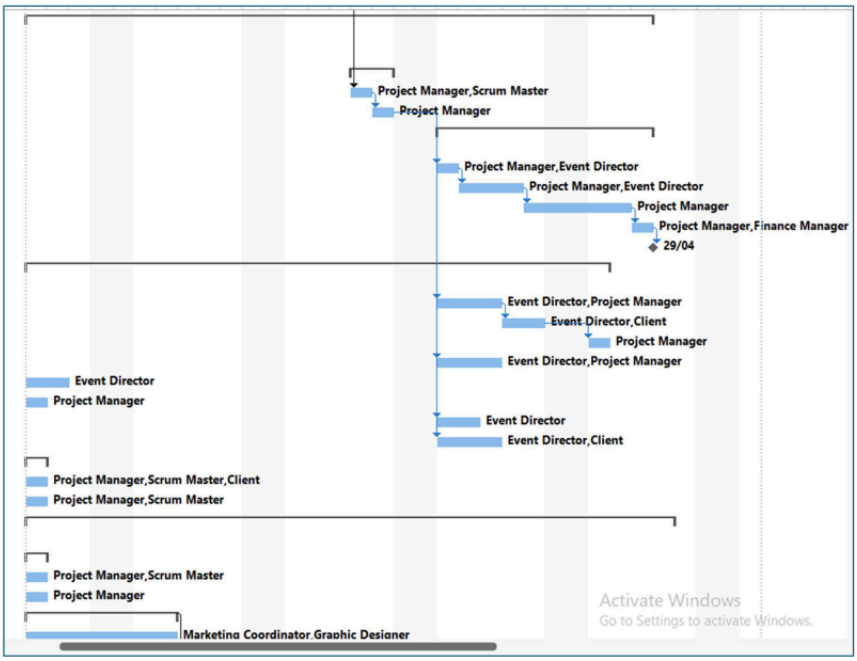
Project Manager,Scrum Master
Project Manager
Project Manager,Event Director
Project Manager,Event Director
Project Manager
Project Manager,Finance Manager
29/04
Event Director,Project Manager
Event Director,Client
Project Manager
Event Director,Project Manager
Event Director
Project Manager
Event Director
Event Director,Client
Project Manager,Scrum Master,Client
Project Manager,Scrum Master
Project Manager,Scrum Master
Project Manager
Marketing Coordinator,Graphic Designer
Activate Windows
Go to Settings to activate Windows.

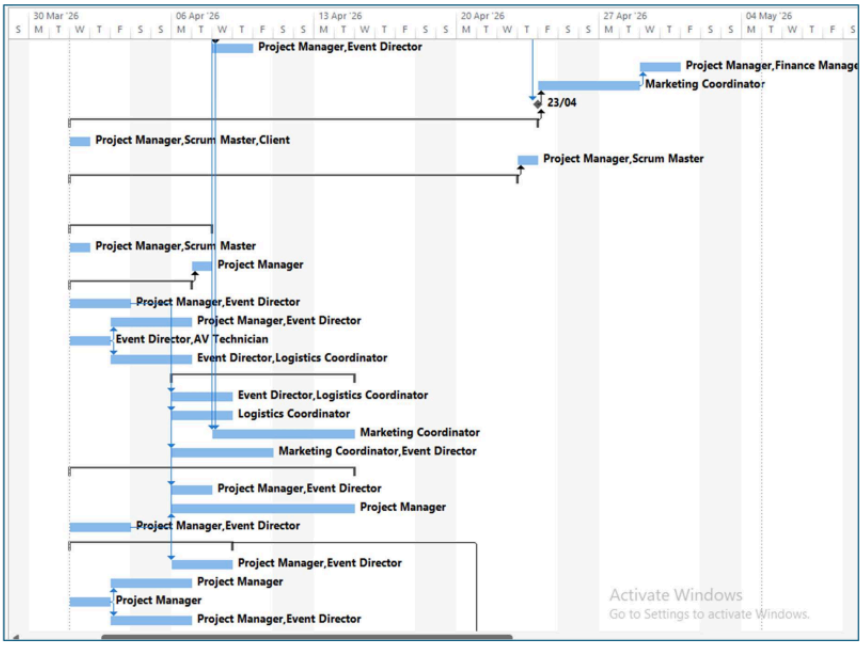

30 Mar '26
06 Apr '26
13 Apr '26
20 Apr '26
27 Apr '26
04 May '26
Project Manager,Event Director
Project Manager,Finance Manage
Marketing Coordinator
23/04
Project Manager,Scrum Master,Client
Project Manager,Scrum Master
Project Manager,Scrum Master
Project Manager
Project Manager,Event Director
Project Manager,Event Director
Event Director,AV Technician
Event Director,Logistics Coordinator
Event Director,Logistics Coordinator
Logistics Coordinator
Marketing Coordinator
Marketing Coordinator,Event Director
Project Manager,Event Director
Project Manager
Project Manager,Event Director
Project Manager,Event Director
Project Manager
Project Manager
Project Manager,Event Director
Activate Windows
Go to Settings to activate Windows.

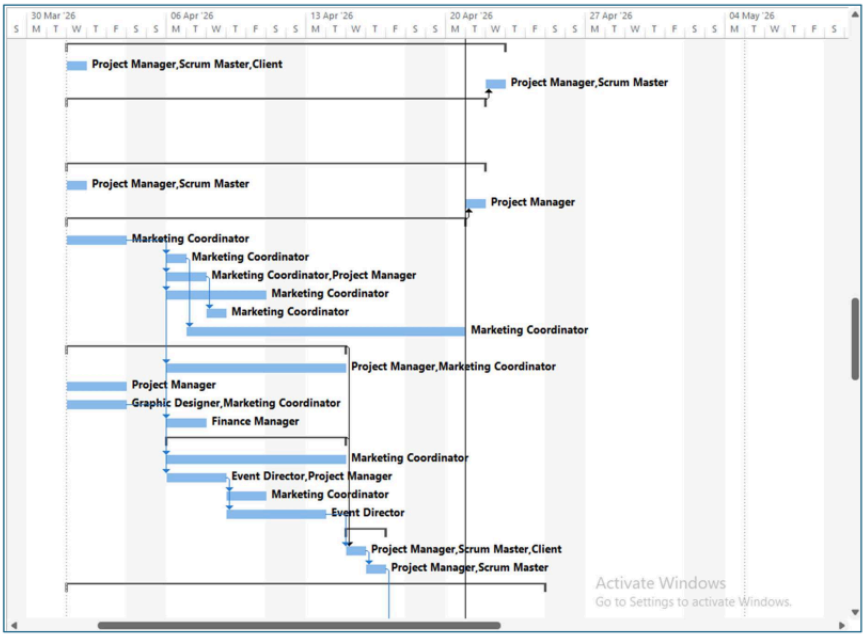

30 Mar '26
06 Apr '26
13 Apr '26
20 Apr '26
27 Apr '26
04 May '26
Project Manager,Scrum Master,Client
Project Manager,Scrum Master
Project Manager,Scrum Master
Project Manager
Marketing Coordinator
Marketing Coordinator
Marketing Coordinator,Project Manager
Marketing Coordinator
Marketing Coordinator
Marketing Coordinator
Project Manager,Marketing Coordinator
Project Manager
Graphic Designer,Marketing Coordinator
Finance Manager
Marketing Coordinator
Event Director,Project Manager
Marketing Coordinator
Event Director
Project Manager,Scrum Master,Client
Project Manager,Scrum Master
Activate Windows
Go to Settings to activate Windows.

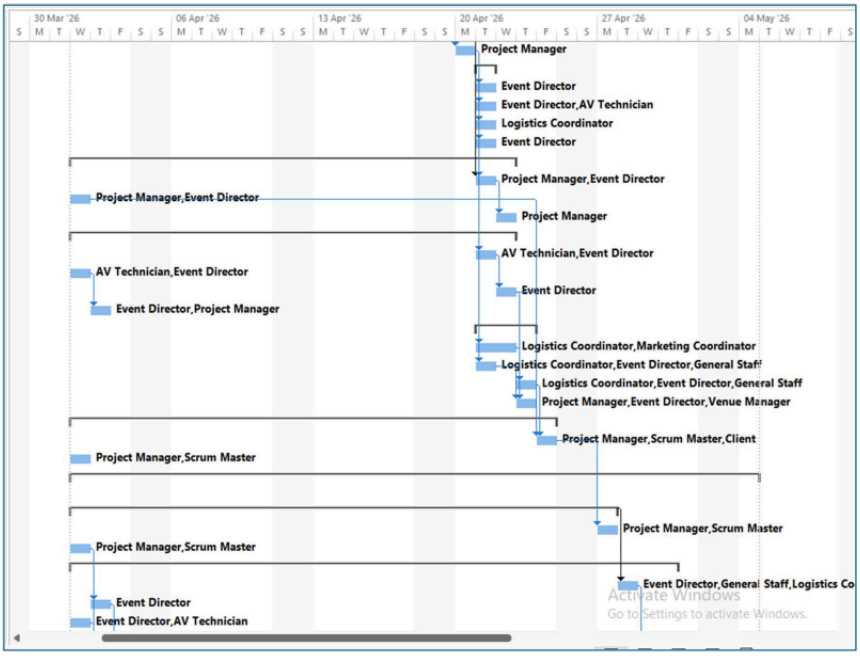

30 Mar '26
06 Apr '26
13 Apr '26
20 Apr '26
27 Apr '26
04 May '26
Project Manager
Event Director
Event Director,AV Technician
Logistics Coordinator
Event Director
Project Manager,Event Director
Project Manager,Event Director
Project Manager
AV Technician,Event Director
Event Director
Event Director,Project Manager
Logistics Coordinator,Marketing Coordinator
Logistics Coordinator,Event Director,General Staff
Logistics Coordinator,Event Director,General Staff
Project Manager,Event Director,Venue Manager
Project Manager,Scrum Master,Client
Project Manager,Scrum Master
Project Manager,Scrum Master
Project Manager,Scrum Master
Event Director,General Staff,Logistics Co
Event Director
Event Director,AV Technician
Activate Windows
Go to Settings to activate Windows.

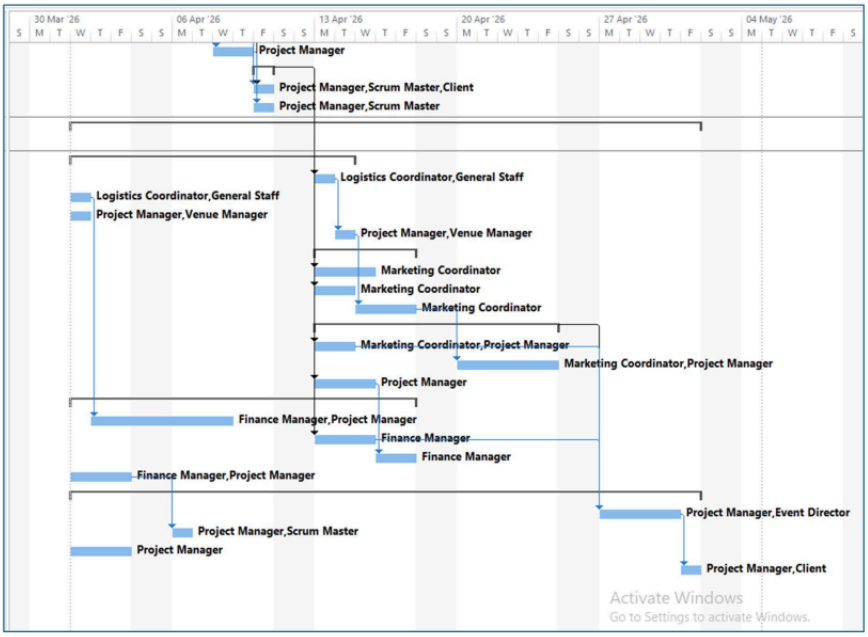


Appendix C — Network Diagram (MS Project Export)

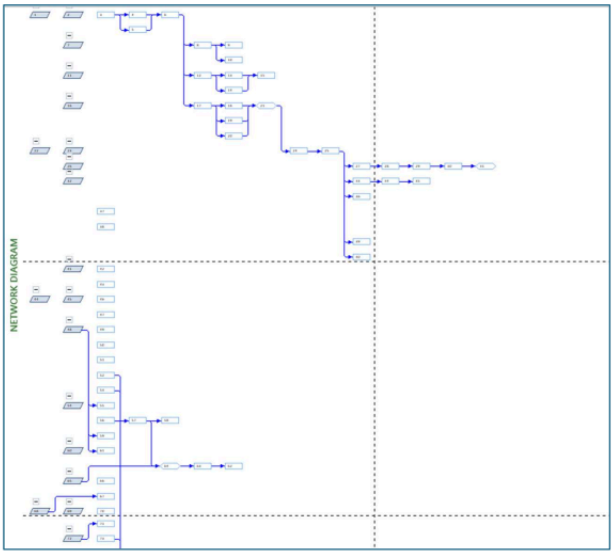

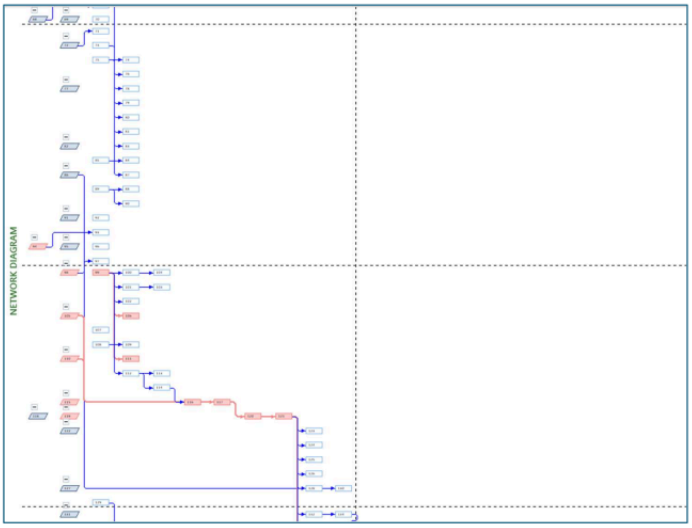

NETWORK DIAGRAM

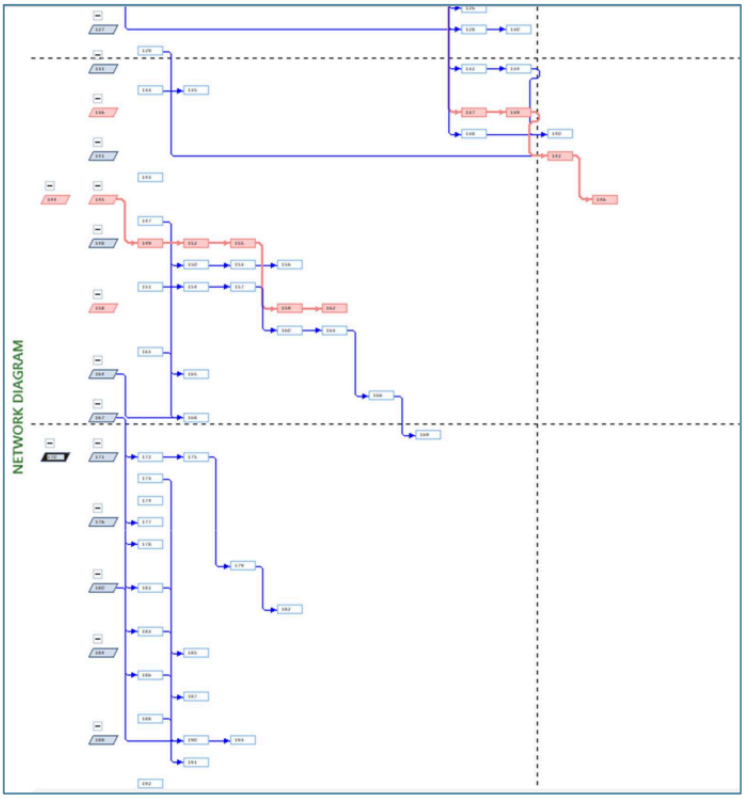
NETWORK DIAGRAM


Appendix D — Resource Usage Report (MS Project Export)

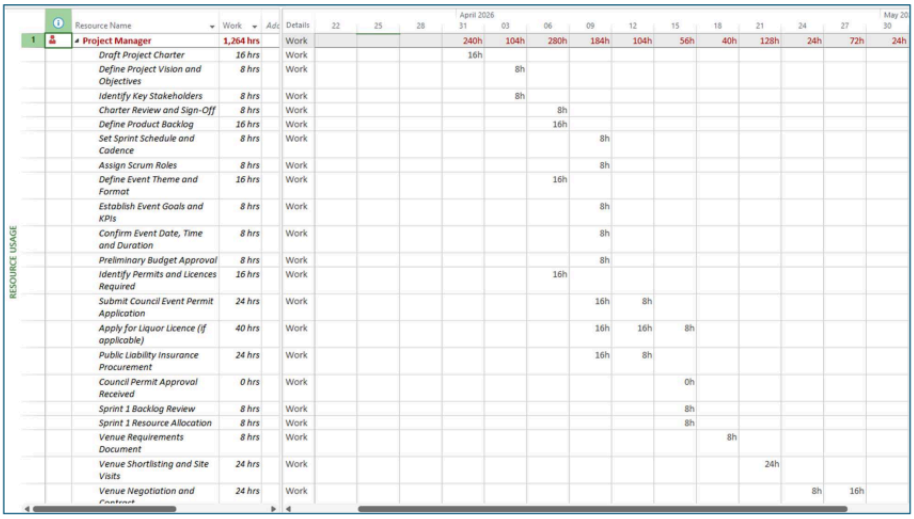


	Resource Name	Work	Adc	Details
1	Project Manager	1,264 hrs		Work
	Draft Project Charter	16 hrs		Work
	Define Project Vision and Objectives	8 hrs		Work
	Identify Key Stakeholders	8 hrs		Work
	Charter Review and Sign-Off	8 hrs		Work
	Define Product Backlog	16 hrs		Work
	Set Sprint Schedule and Cadence	8 hrs		Work
	Assign Scrum Roles	8 hrs		Work
	Define Event Theme and Format	16 hrs		Work
	Establish Event Goals and KPIs	8 hrs		Work
	Confirm Event Date, Time and Duration	8 hrs		Work
	Preliminary Budget Approval	8 hrs		Work
	Identify Permits and Licences Required	16 hrs		Work
	Submit Council Event Permit Application	24 hrs		Work
	Apply for Liquor Licence (if applicable)	40 hrs		Work
	Public Liability Insurance Procurement	24 hrs		Work
	Council Permit Approval Received	0 hrs		Work
	Sprint 1 Backlog Review	8 hrs		Work
	Sprint 1 Resource Allocation	8 hrs		Work
	Venue Requirements Document	8 hrs		Work
	Venue Shortlisting and Site Visits	24 hrs		Work
	Venue Negotiation and Contract	24 hrs		Work

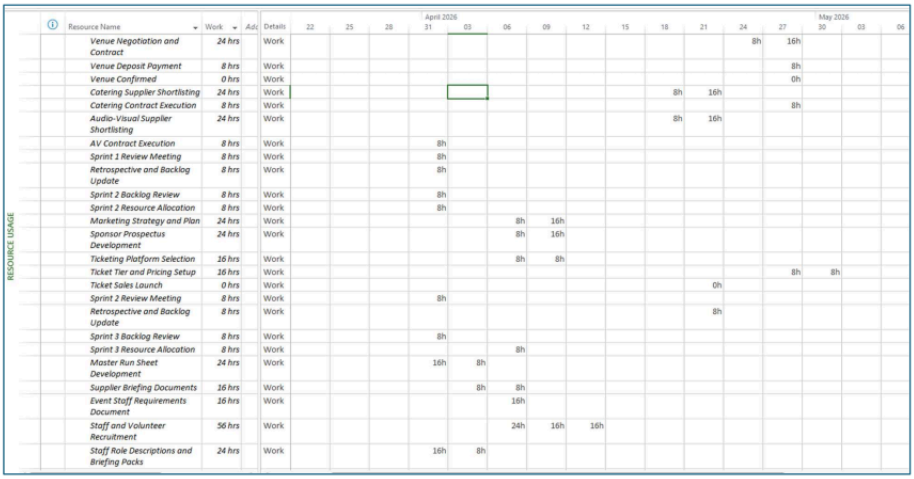


	Resource Name	Work	Adc	Details
	Venue Negotiation and Contract	24 hrs		Work
	Venue Deposit Payment	8 hrs		Work
	Venue Confirmed	0 hrs		Work
	Catering Supplier Shortlisting	24 hrs		Work
	Catering Contract Execution	8 hrs		Work
	Audio-Visual Supplier Shortlisting	24 hrs		Work
	AV Contract Execution	8 hrs		Work
	Sprint 1 Review Meeting	8 hrs		Work
	Retrospective and Backlog Update	8 hrs		Work
	Sprint 2 Backlog Review	8 hrs		Work
	Sprint 2 Resource Allocation	8 hrs		Work
	Marketing Strategy and Plan	24 hrs		Work
	Sponsor Prospectus Development	24 hrs		Work
	Ticketing Platform Selection	16 hrs		Work
	Ticket Tier and Pricing Setup	16 hrs		Work
	Ticket Sales Launch	0 hrs		Work
	Sprint 2 Review Meeting	8 hrs		Work
	Retrospective and Backlog Update	8 hrs		Work
	Sprint 3 Backlog Review	8 hrs		Work
	Sprint 3 Resource Allocation	8 hrs		Work
	Master Run Sheet Development	24 hrs		Work
	Supplier Briefing Documents	16 hrs		Work
	Event Staff Requirements Document	16 hrs		Work
	Staff and Volunteer Recruitment	56 hrs		Work
	Staff Role Descriptions and Briefing Packs	24 hrs		Work

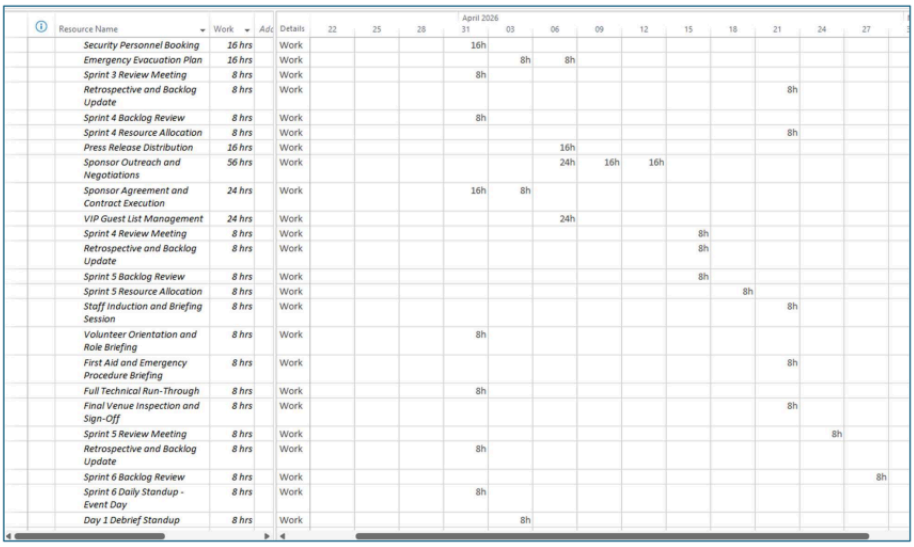


Resource Name	Work	Adc	Details	22	25	28	31	03	06	09	12	15	18	21	24	27
				April 2026												
Security Personnel Booking	16 hrs		Work				16h									
Emergency Evacuation Plan	16 hrs		Work					8h	8h							
Sprint 3 Review Meeting	8 hrs		Work				8h									
Retrospective and Backlog Update	8 hrs		Work											8h		
Sprint 4 Backlog Review	8 hrs		Work				8h									
Sprint 4 Resource Allocation	8 hrs		Work											8h		
Press Release Distribution	16 hrs		Work						16h							
Sponsor Outreach and Negotiations	56 hrs		Work						24h	16h	16h					
Sponsor Agreement and Contract Execution	24 hrs		Work				16h	8h								
VIP Guest List Management	24 hrs		Work						24h							
Sprint 4 Review Meeting	8 hrs		Work									8h				
Retrospective and Backlog Update	8 hrs		Work									8h				
Sprint 5 Backlog Review	8 hrs		Work									8h				
Sprint 5 Resource Allocation	8 hrs		Work										8h			
Staff Induction and Briefing Session	8 hrs		Work											8h		
Volunteer Orientation and Role Briefing	8 hrs		Work				8h									
First Aid and Emergency Procedure Briefing	8 hrs		Work											8h		
Full Technical Run-Through	8 hrs		Work				8h									
Final Venue Inspection and Sign-Off	8 hrs		Work											8h		
Sprint 5 Review Meeting	8 hrs		Work												8h	
Retrospective and Backlog Update	8 hrs		Work				8h									
Sprint 6 Backlog Review	8 hrs		Work													8h
Sprint 6 Daily Standup - Event Day	8 hrs		Work				8h									
Day 1 Debrief Standup	8 hrs		Work					8h								

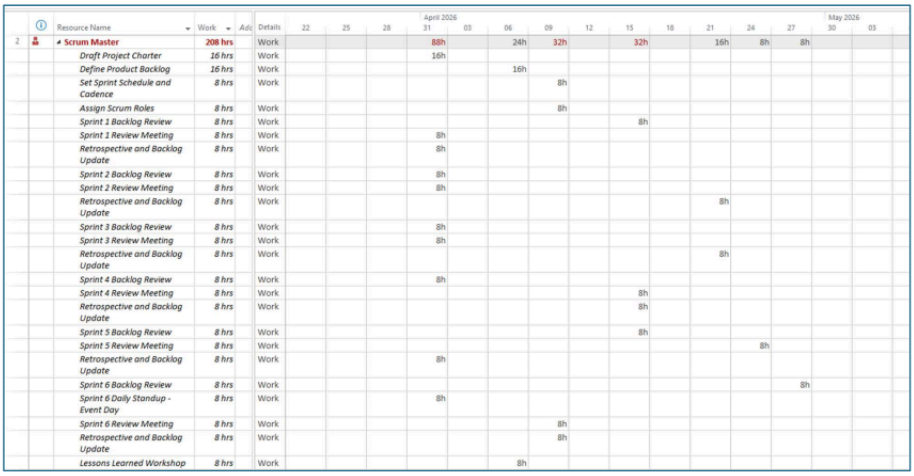


	Resource Name	Work	Adc	Details	22	25	28	31	03	06	09	12	15	18	21	24	27	30	03
					April 2026													May 2026	
2	Scrum Master	208 hrs		Work				88h		24h	32h		32h		16h	8h	8h		
	Draft Project Charter	16 hrs		Work				16h											
	Define Product Backlog	16 hrs		Work						16h									
	Set Sprint Schedule and Cadence	8 hrs		Work							8h								
	Assign Scrum Roles	8 hrs		Work							8h								
	Sprint 1 Backlog Review	8 hrs		Work									8h						
	Sprint 1 Review Meeting	8 hrs		Work				8h											
	Retrospective and Backlog Update	8 hrs		Work				8h											
	Sprint 2 Backlog Review	8 hrs		Work				8h											
	Sprint 2 Review Meeting	8 hrs		Work				8h											
	Retrospective and Backlog Update	8 hrs		Work											8h				
	Sprint 3 Backlog Review	8 hrs		Work				8h											
	Sprint 3 Review Meeting	8 hrs		Work				8h											
	Retrospective and Backlog Update	8 hrs		Work											8h				
	Sprint 4 Backlog Review	8 hrs		Work				8h											
	Sprint 4 Review Meeting	8 hrs		Work									8h						
	Retrospective and Backlog Update	8 hrs		Work									8h						
	Sprint 5 Backlog Review	8 hrs		Work									8h						
	Sprint 5 Review Meeting	8 hrs		Work												8h			
	Retrospective and Backlog Update	8 hrs		Work				8h											
	Sprint 6 Backlog Review	8 hrs		Work													8h		
	Sprint 6 Daily Standup - Event Day	8 hrs		Work				8h											
	Sprint 6 Review Meeting	8 hrs		Work							8h								
	Retrospective and Backlog Update	8 hrs		Work							8h								
	Lessons Learned Workshop	8 hrs		Work						8h									

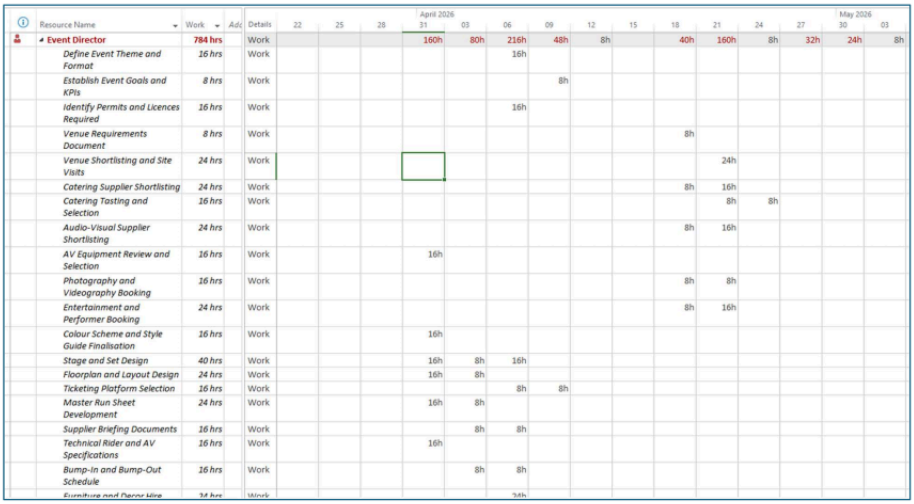


Resource Name	Work	Details	22	25	28	31	03	06	09	12	15	18	21	24	27	30	03
			April 2026													May 2026	
Event Director	784 hrs	Work				160h	80h	216h	48h	8h		40h	160h	8h	32h	24h	8h
Define Event Theme and Format	16 hrs	Work						16h									
Establish Event Goals and KPIs	8 hrs	Work							8h								
Identify Permits and Licences Required	16 hrs	Work						16h									
Venue Requirements Document	8 hrs	Work										8h					
Venue Shortlisting and Site Visits	24 hrs	Work											24h				
Catering Supplier Shortlisting	24 hrs	Work										8h	16h				
Catering Tasting and Selection	16 hrs	Work											8h	8h			
Audio-Visual Supplier Shortlisting	24 hrs	Work										8h	16h				
AV Equipment Review and Selection	16 hrs	Work				16h											
Photography and Videography Booking	16 hrs	Work										8h	8h				
Entertainment and Performer Booking	24 hrs	Work										8h	16h				
Colour Scheme and Style Guide Finalisation	16 hrs	Work				16h											
Stage and Set Design	40 hrs	Work				16h	8h	16h									
Floorplan and Layout Design	24 hrs	Work				16h	8h										
Ticketing Platform Selection	16 hrs	Work						8h	8h								
Master Run Sheet Development	24 hrs	Work				16h	8h										
Supplier Briefing Documents	16 hrs	Work					8h	8h									
Technical Rider and AV Specifications	16 hrs	Work				16h											
Bump-In and Bump-Out Schedule	16 hrs	Work					8h	8h									
Furniture and Decor Hire	24 hrs	Work						24h									

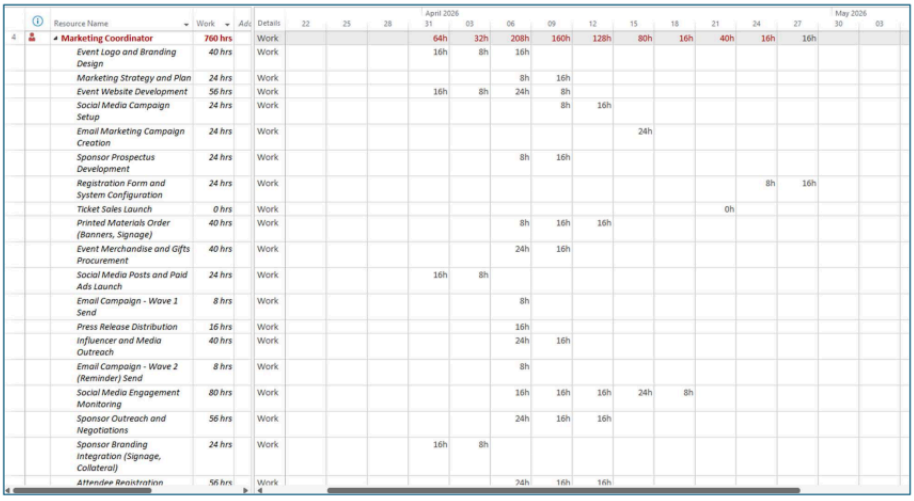


Resource Name	Work	Details	22	25	28	31	03	06	09	12	15	18	21	24	27	30	03
			April 2026													May 2026	
Marketing Coordinator	760 hrs	Work				64h	32h	208h	160h	128h	80h	16h	40h	16h	16h		
Event Logo and Branding Design	40 hrs	Work				16h	8h	16h									
Marketing Strategy and Plan	24 hrs	Work						8h	16h								
Event Website Development	56 hrs	Work				16h	8h	24h	8h								
Social Media Campaign Setup	24 hrs	Work							8h	16h							
Email Marketing Campaign Creation	24 hrs	Work									24h						
Sponsor Prospectus Development	24 hrs	Work						8h	16h								
Registration Form and System Configuration	24 hrs	Work												8h	16h		
Ticket Sales Launch	0 hrs	Work											0h				
Printed Materials Order (Banners, Signage)	40 hrs	Work						8h	16h	16h							
Event Merchandise and Gifts Procurement	40 hrs	Work						24h	16h								
Social Media Posts and Paid Ads Launch	24 hrs	Work				16h	8h										
Email Campaign - Wave 1 Send	8 hrs	Work						8h									
Press Release Distribution	16 hrs	Work						16h									
Influencer and Media Outreach	40 hrs	Work						24h	16h								
Email Campaign - Wave 2 (Reminder) Send	8 hrs	Work						8h									
Social Media Engagement Monitoring	80 hrs	Work						16h	16h	16h	24h	8h					
Sponsor Outreach and Negotiations	56 hrs	Work						24h	16h	16h							
Sponsor Branding Integration (Signage, Collateral)	24 hrs	Work				16h	8h										
Attendee Registration	56 hrs	Work						24h	16h	16h							

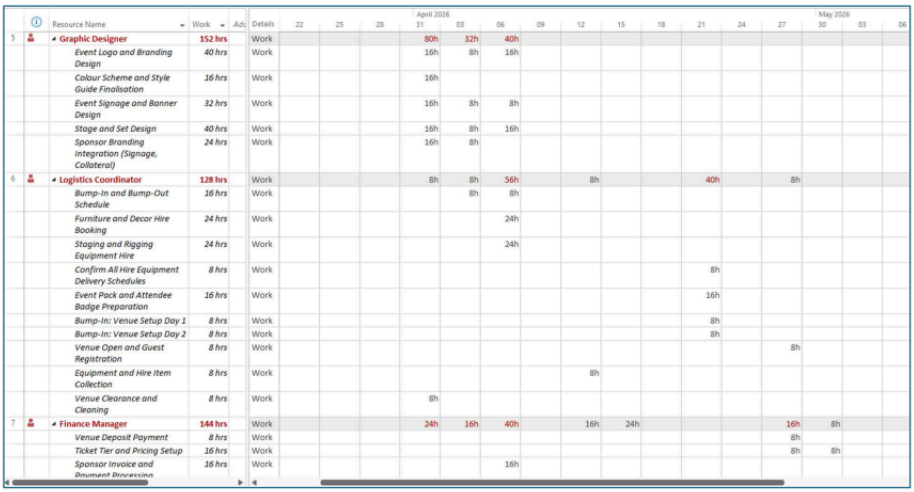

	Resource Name	Work	Details	22	25	28	31	03	06	09	12	15	18	21	24	27	30	03	06
				April 2026													May 2026		
5	Graphic Designer	152 hrs	Work				80h	32h	40h										
	Event Logo and Branding Design	40 hrs	Work				16h	8h	16h										
	Colour Scheme and Style Guide Finalisation	16 hrs	Work				16h												
	Event Signage and Banner Design	32 hrs	Work				16h	8h	8h										
	Stage and Set Design	40 hrs	Work				16h	8h	16h										
	Sponsor Branding Integration (Signage, Collateral)	24 hrs	Work				16h	8h											
6	Logistics Coordinator	128 hrs	Work				8h	8h	56h		8h			40h		8h			
	Bump-In and Bump-Out Schedule	16 hrs	Work					8h	8h										
	Furniture and Decor Hire Booking	24 hrs	Work						24h										
	Staging and Rigging Equipment Hire	24 hrs	Work						24h										
	Confirm All Hire Equipment Delivery Schedules	8 hrs	Work											8h					
	Event Pack and Attendee Badge Preparation	16 hrs	Work											16h					
	Bump-In: Venue Setup Day 1	8 hrs	Work											8h					
	Bump-In: Venue Setup Day 2	8 hrs	Work											8h					
	Venue Open and Guest Registration	8 hrs	Work													8h			
	Equipment and Hire Item Collection	8 hrs	Work								8h								
	Venue Clearance and Cleaning	8 hrs	Work				8h												
7	Finance Manager	144 hrs	Work				24h	16h	40h		16h	24h				16h	8h		
	Venue Deposit Payment	8 hrs	Work													8h			
	Ticket Tier and Pricing Setup	16 hrs	Work													8h	8h		
	Sponsor Invoice and Payment Processing	16 hrs	Work						16h										

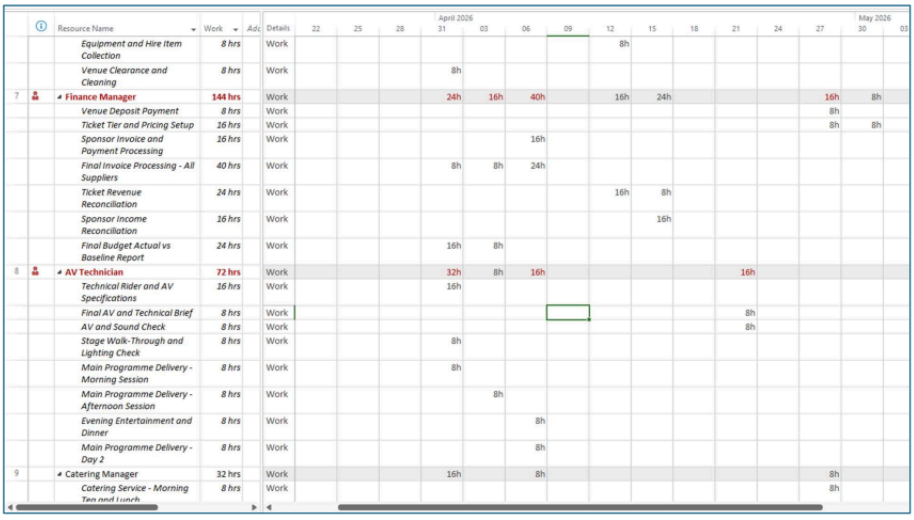

	Resource Name	Work	Details	22	25	28	31	03	06	09	12	15	18	21	24	27	30	03
				April 2026													May 2026	
	Equipment and Hire Item Collection	8 hrs	Work								8h							
	Venue Clearance and Cleaning	8 hrs	Work				8h											
7	Finance Manager	144 hrs	Work				24h	16h	40h		16h	24h				16h	8h	
	Venue Deposit Payment	8 hrs	Work													8h		
	Ticket Tier and Pricing Setup	16 hrs	Work													8h	8h	
	Sponsor Invoice and Payment Processing	16 hrs	Work						16h									
	Final Invoice Processing - All Suppliers	40 hrs	Work				8h	8h	24h									
	Ticket Revenue Reconciliation	24 hrs	Work								16h	8h						
	Sponsor Income Reconciliation	16 hrs	Work									16h						
	Final Budget Actual vs Baseline Report	24 hrs	Work				16h	8h										
8	AV Technician	72 hrs	Work				32h	8h	16h						16h			
	Technical Rider and AV Specifications	16 hrs	Work				16h											
	Final AV and Technical Brief	8 hrs	Work												8h			
	AV and Sound Check	8 hrs	Work												8h			
	Stage Walk-Through and Lighting Check	8 hrs	Work				8h											
	Main Programme Delivery - Morning Session	8 hrs	Work				8h											
	Main Programme Delivery - Afternoon Session	8 hrs	Work					8h										
	Evening Entertainment and Dinner	8 hrs	Work						8h									
	Main Programme Delivery - Day 2	8 hrs	Work						8h									
9	Catering Manager	32 hrs	Work				16h		8h								8h	
	Catering Service - Morning Tea and Lunch	8 hrs	Work														8h	

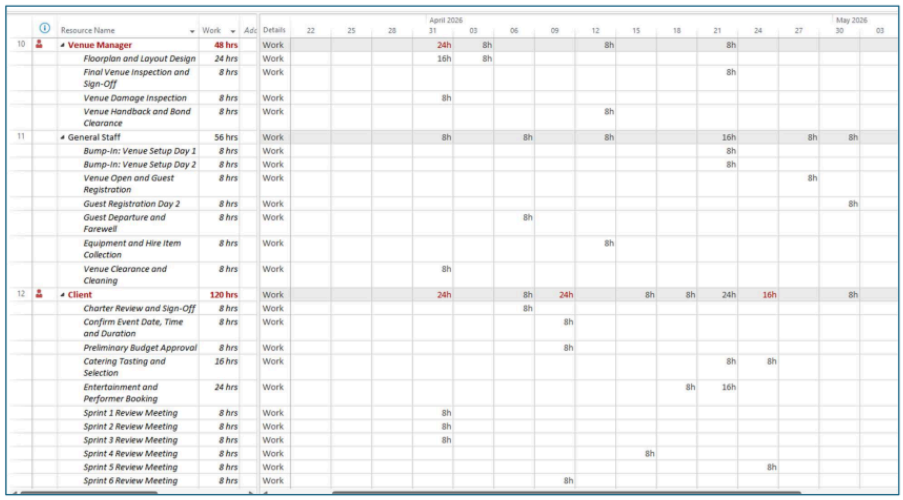

	Resource Name	Work	Details	April 2026 22	25	28	31	03	06	09	12	15	18	21	24	27	May 2026 30	03
10	Venue Manager	48 hrs	Work				24h	8h			8h			8h				
	Floorplan and Layout Design	24 hrs	Work				16h	8h										
	Final Venue Inspection and Sign-Off	8 hrs	Work											8h				
	Venue Damage Inspection	8 hrs	Work				8h											
	Venue Handback and Bond Clearance	8 hrs	Work								8h							
11	General Staff	56 hrs	Work				8h		8h		8h			16h		8h	8h	
	Bump-In: Venue Setup Day 1	8 hrs	Work											8h				
	Bump-In: Venue Setup Day 2	8 hrs	Work											8h				
	Venue Open and Guest Registration	8 hrs	Work													8h		
	Guest Registration Day 2	8 hrs	Work														8h	
	Guest Departure and Farewell	8 hrs	Work						8h									
	Equipment and Hire Item Collection	8 hrs	Work								8h							
	Venue Clearance and Cleaning	8 hrs	Work				8h											
12	Client	120 hrs	Work				24h		8h	24h		8h	8h	24h	16h		8h	
	Charter Review and Sign-Off	8 hrs	Work						8h									
	Confirm Event Date, Time and Duration	8 hrs	Work							8h								
	Preliminary Budget Approval	8 hrs	Work							8h								
	Catering Tasting and Selection	16 hrs	Work											8h	8h			
	Entertainment and Performer Booking	24 hrs	Work										8h	16h				
	Sprint 1 Review Meeting	8 hrs	Work				8h											
	Sprint 2 Review Meeting	8 hrs	Work				8h											
	Sprint 3 Review Meeting	8 hrs	Work				8h											
	Sprint 4 Review Meeting	8 hrs	Work									8h						
	Sprint 5 Review Meeting	8 hrs	Work												8h			
	Sprint 6 Review Meeting	8 hrs	Work							8h								

Appendix E — Source File Reference

EventManagement_Agile.mpp — Microsoft Project source file.

Agile_EventManagement_ProjectPlan_4000w

ORIGINALITY REPORT

4%	3%	2%	3%
SIMILARITY INDEX	INTERNET SOURCES	PUBLICATIONS	STUDENT PAPERS

PRIMARY SOURCES

1	cdmbuntu.lib.utah.edu Internet Source	1%
2	Submitted to Futureskills Academy Student Paper	1%
3	pdfcoffee.com Internet Source	<1%
4	Submitted to Global Banking Training Student Paper	<1%
5	Submitted to Dublin Business School Student Paper	<1%
6	www.accountablehq.com Internet Source	<1%
7	www.energy.gov Internet Source	<1%
8	Paul Sanghera. "CAPM® in Depth", Springer Science and Business Media LLC, 2019 Publication	<1%
9	ebin.pub Internet Source	<1%

Exclude quotes On

Exclude matches Off

Exclude bibliography On
